VCBC CPR

PROJECT UPDATE
最新消息

SEPTEMBER 2026

CONCEPT PLANS • FUNDING OUTLOOK • DECISION GATES

ARCHITECTURAL PLANS

Site & ground-level plan 主層

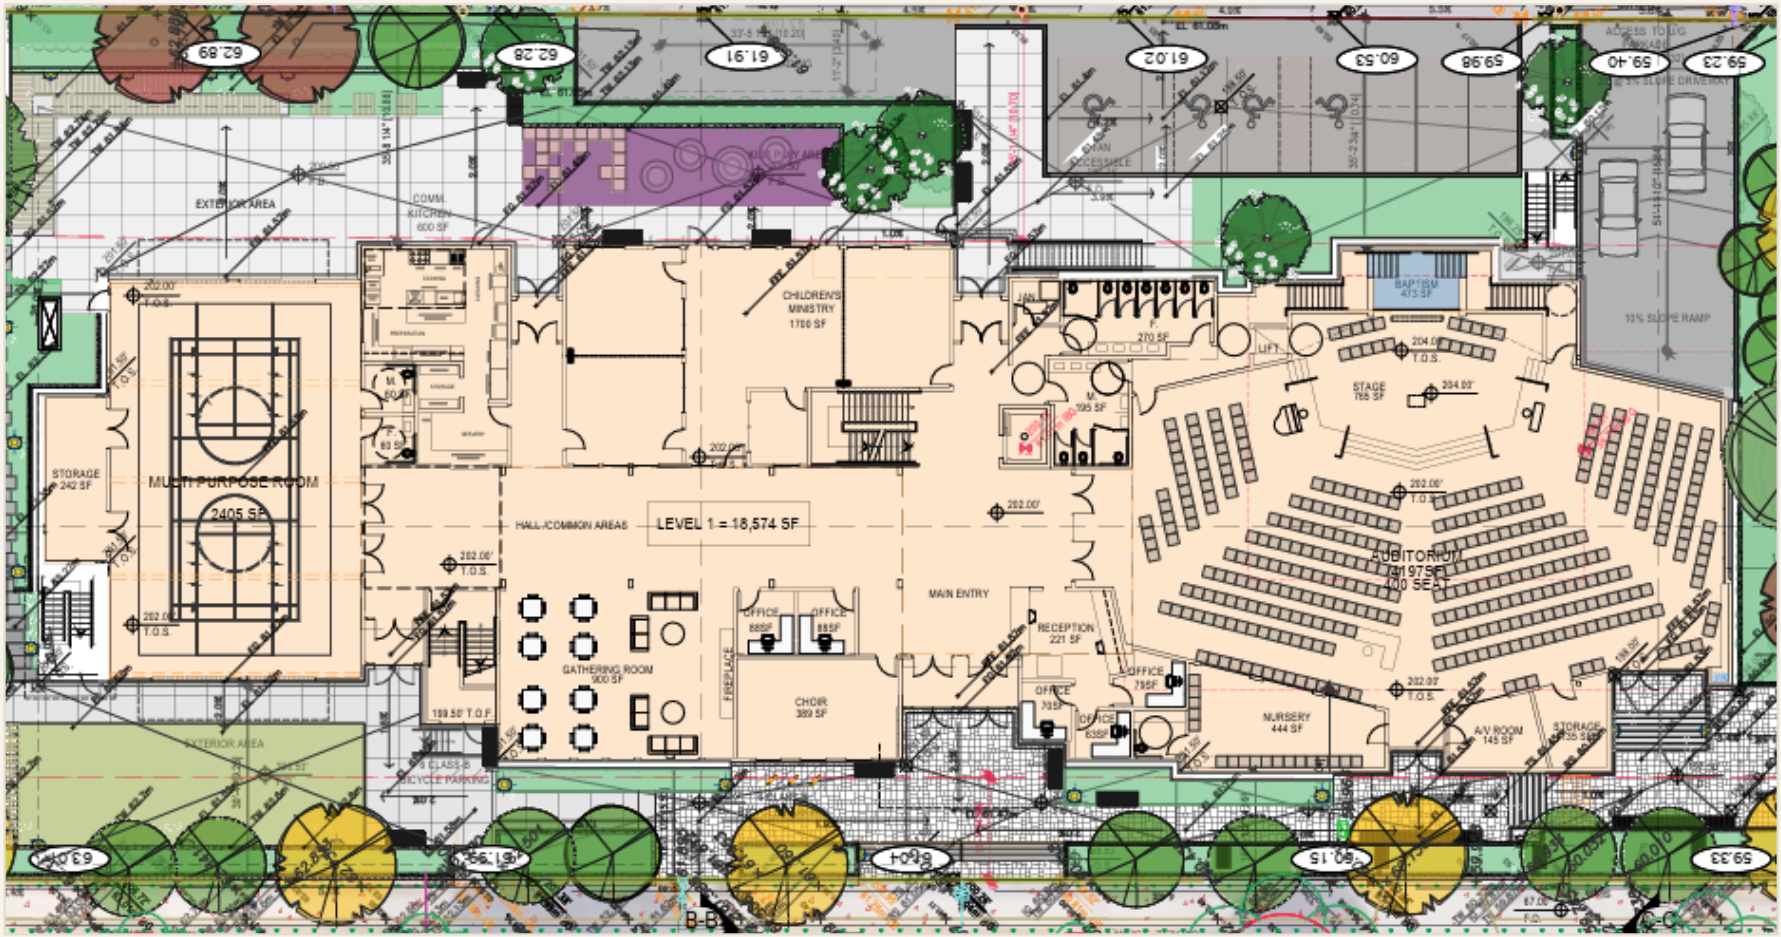

ARCHITECTURAL PLANS

Upper Floor Plan 上層

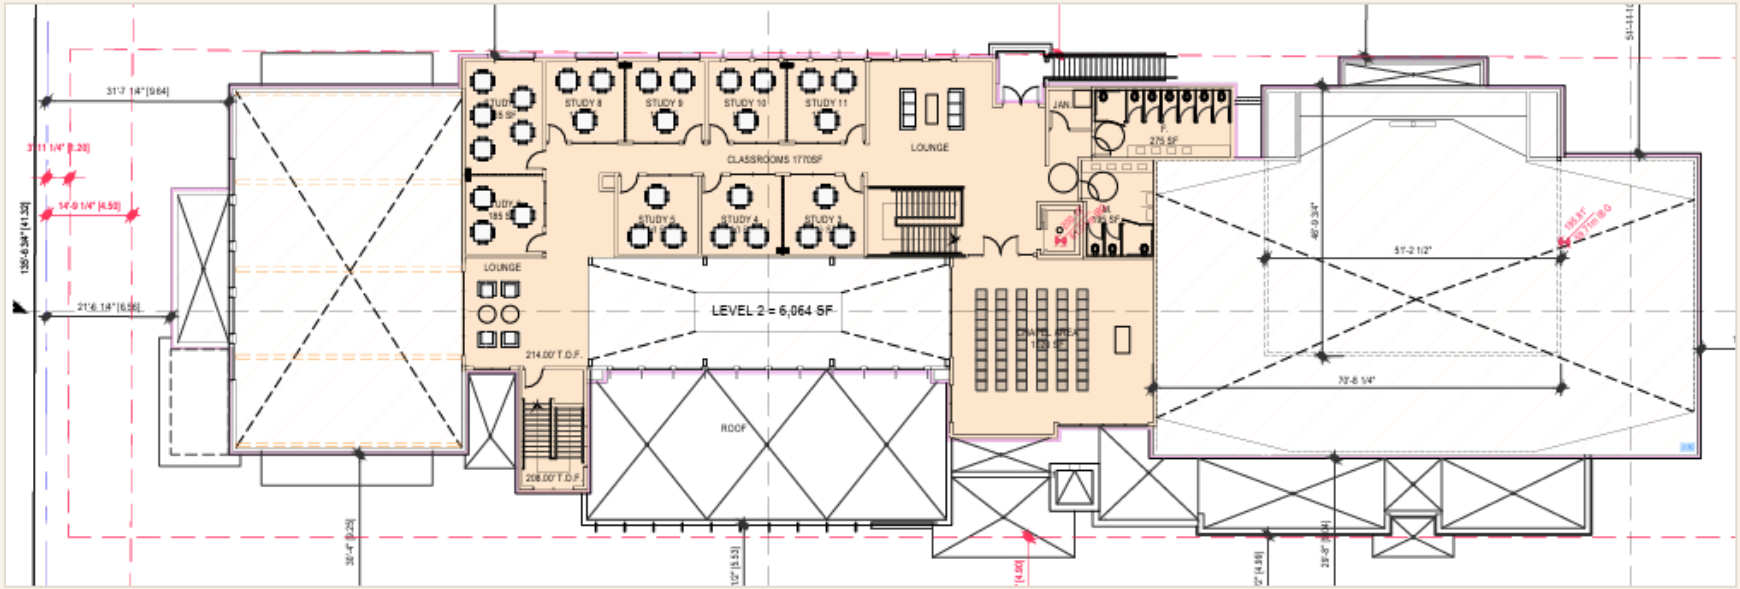

Retained design
保留原有設計

Patio Removed
移除室外閣樓

ARCHITECTURAL PLANS

Underground Parking Plan 停車場

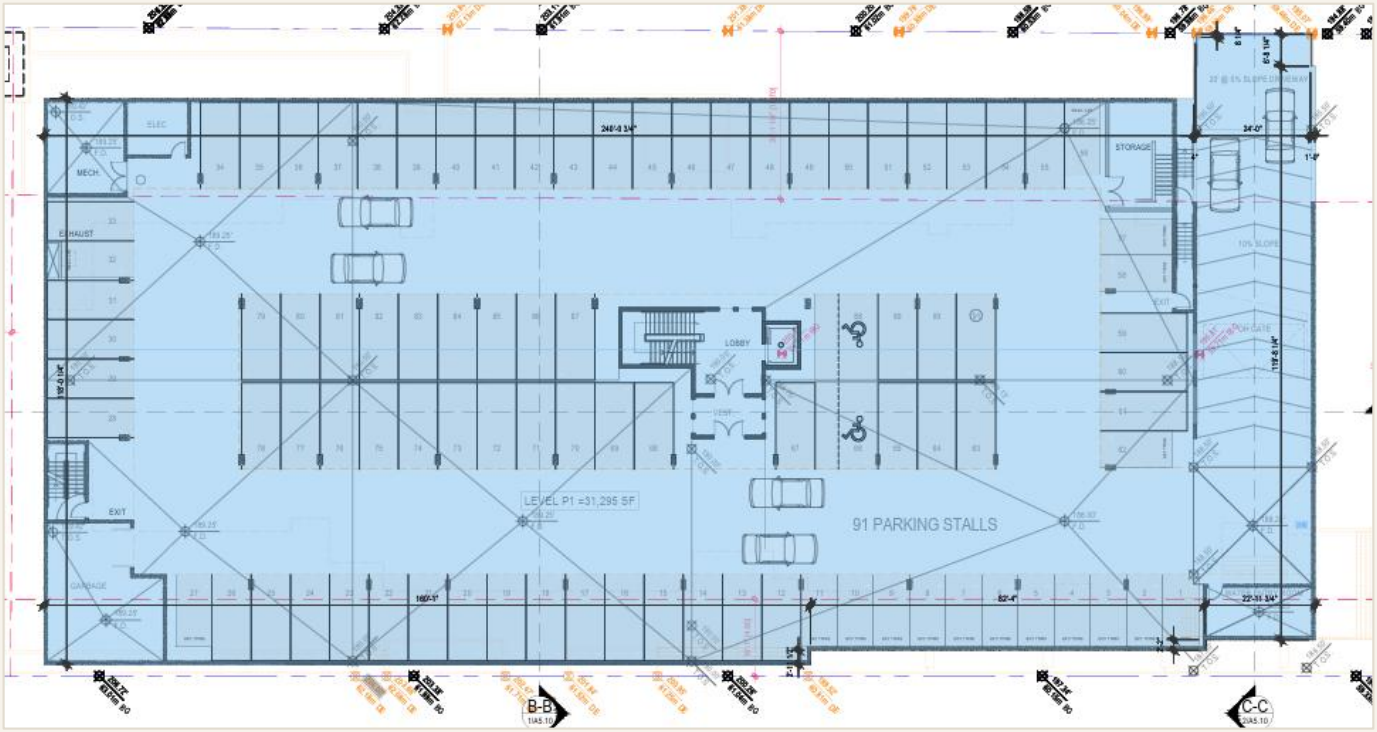

City approved stall reduction (20 spots)
市政府批准削減20個車位

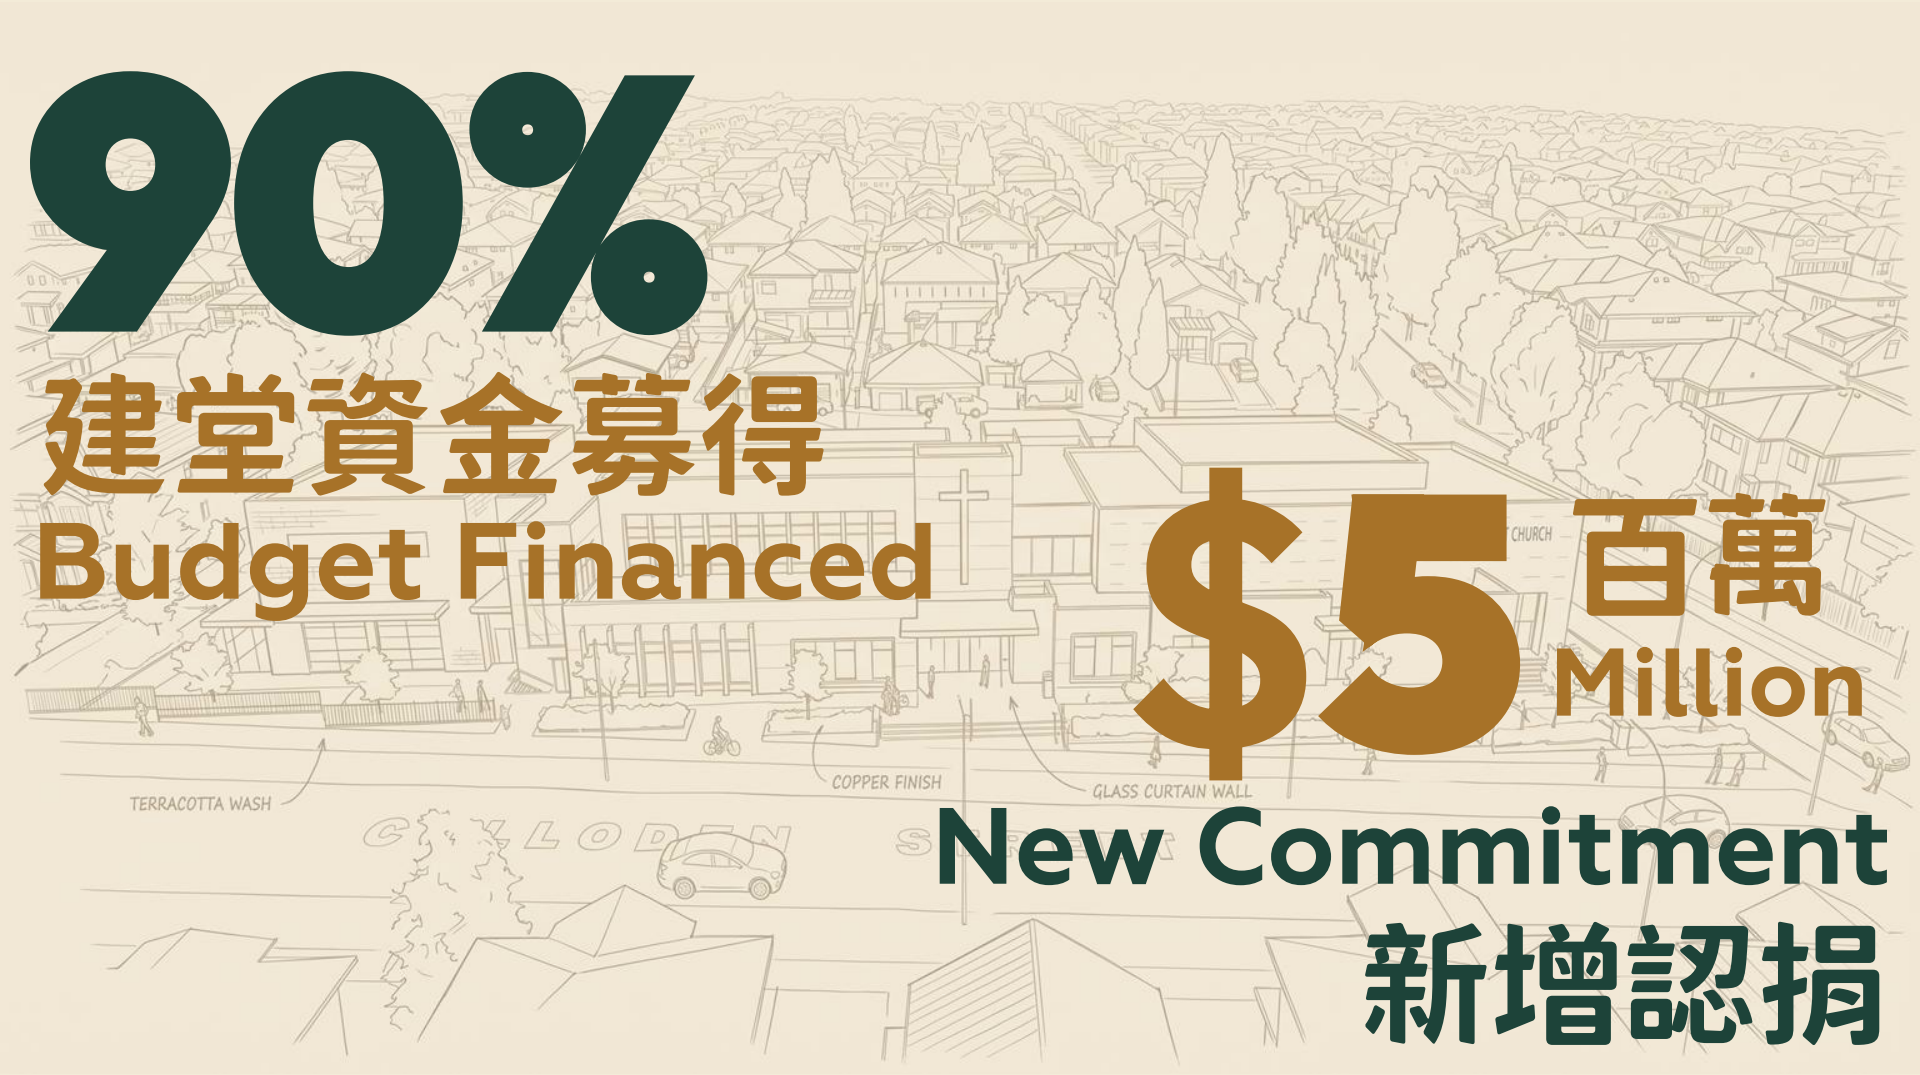

90%

建堂資金募得

Budget Financed

$5 百萬 Million

New Commitment

新增認捐

Fundraising

MAJOR PROGRESS重要籌款進展

現有建築資金

Cash available to construction

$20.8M

Committed sources

Cash on hand · Dec 31, 2025	**$8.9M**
Pledge receivable	**$2.5M**
F'2026 received to date	**$0.8M**
Sparkler loan	**$4.2M**
New commitment	**$5.0M**
Less cost to complete BP	**–$0.6M**

預計 Estimated Construction Cost 所需建築成本

$23.0M

尚需要款項 **$2.2M**

Remaining shortfall

*after BP Application costs

新的建堂籌款目標
New Fundraising Target

$20.8M Raised (90%)

*Rounded up from the $2.2M shortfall

建堂計畫時間表
Project Schedul

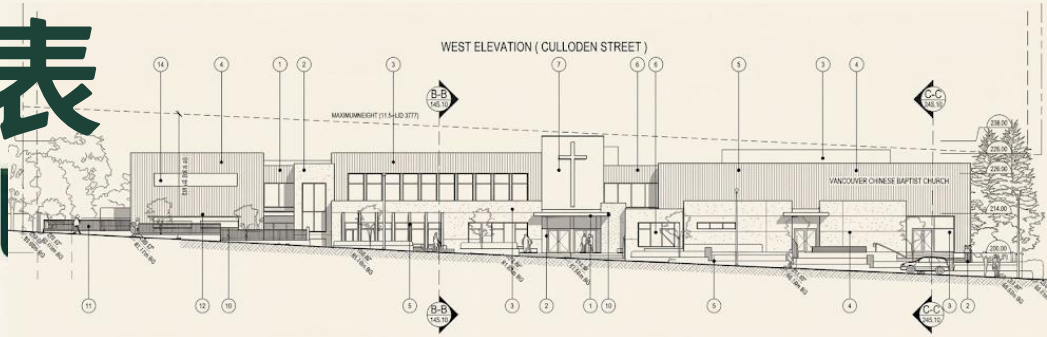

Dec 2026
BP submitted
申請建築牌照

Mar 2027
BP approved + drawings 100% complete
獲取牌照及確定圖則

Mar–Jun 2027
Temporary site lease executed
確定臨時租用場地

May 2027
GC selected + budget finalized
揀選承建商，確定預算

Jun 2027
SAGM approval
特別會友大會動議

Jul 2027
GC contract executed
與承建商正式簽約

Sep 2027
Move complete
完成搬遷

Oct 2027
Demolition starts
正式動土
